


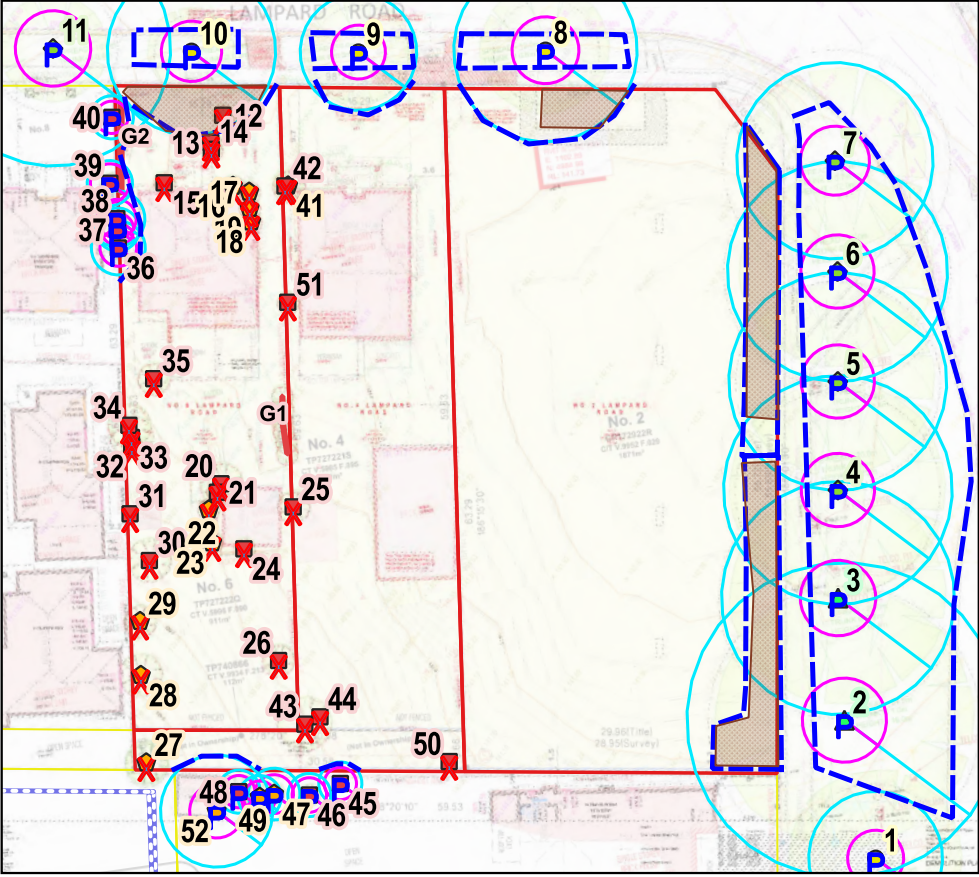

Tree status

P

Protect

X

To be removed

GRD BUFFER

Tree Protection Fencing (TPF)

Notional Root Zone

Structural Root Zone

GENERAL TREE PROTECTION

- The importance of tree protection must be conveyed to all site workers and there must be no entry to fenced TPZ areas without authorisation from the Project Arborist.
- No vehicular access is to occur within the Tree Protection Zone (without adequate ground protection applied).
- No storage or dumping of tools, spoil, equipment, materials, site sheds or waste is to occur within the Tree Protection Zone.
- The Project Arborist must be contacted by the project manager or builder should any unforeseen tree-related issues arise during the development to allow an inspection to be undertaken. Any recommendations made as a result of tree inspections must be carried out in the timeframe and manner specified by the project arborist after the inspection.
- It is the responsibility of the site manager to implement the TMP.
- Tree protection fencing is to be inspected on a daily basis by the site supervisor and maintained in good order.

APPENDIX 2B
TREE PROTECTION PLAN - COVER PAGE

PROJECT
2-6 Lampard Road, Drouin

TL REF. 013416	Version 2	DATE 2026-06-02	CLIENT Housing Choices Australia
-------------------	--------------	--------------------	--



Figure 1. Steel mesh fencing is to be 1.8m temporary fence with weighted feet. Each panel is to be fastened together to deter entry and movement. Signage must be placed on the fencing and be clearly visible, reading "Tree Protection Zone". Fencing may be replaced with suitable trunk and ground protection system under guidance from the Project Arborist.

LANDSCAPING

- TPZ fencing and/or ground protection can be temporarily dismantled for landscaping adjacent to retained trees. Any works within 3 metres of a tree trunk must be undertaken with hand tools.
- The existing soil grade is to be maintained, with only minor surface adjustment to level acceptable (unless discussed with the Project Arborist).
- There must be no compaction of the soil within the TPZ of any retained tree. Oxygen and water must be able to diffuse into the natural soil beneath any new paths or surfaces.
- Irrigation or drainage is not to be trenched within the SRZ and main irrigation lines should be routed outside of TPZ. Laterals can be laid under a thin topdressing of soil and mulch within TPZ.
- Placement of plants may require minor adjust to ensure roots no greater than 30 mm Ø are damaged during planting.

TREE PRUNING

- All pruning requirements must be first discussed with the project arborist who will determine whether the tree can tolerate the works and provide advice on remedial actions, if required.
- Any required pruning must be undertaken by a qualified climbing arborist in accordance with AS4373 – Pruning of Amenity Trees.

SERVICES

- Any requirement to align services through the TPZ of any retained tree must either be bored under the TPZ or installed with hydro excavation under the supervision of the project arborist. No services are permitted in the SRZ of any tree (unless bored).
- No open-cut trenching is to take place within designated TPZ of any retained tree.

ACRONYMS

- TPZ: Tree Protection Zone
- NRZ: Notional root Zone
- SRZ: Structural root zone
- DBH: Diameter at breast height
- NDD: Non-destructive digging
- NDRI: Non-destructive root investigation
- NDD: Non-destructive digging

TPS Codes

- AS: Arborist supervision
- RSD: Root-senstive Construction

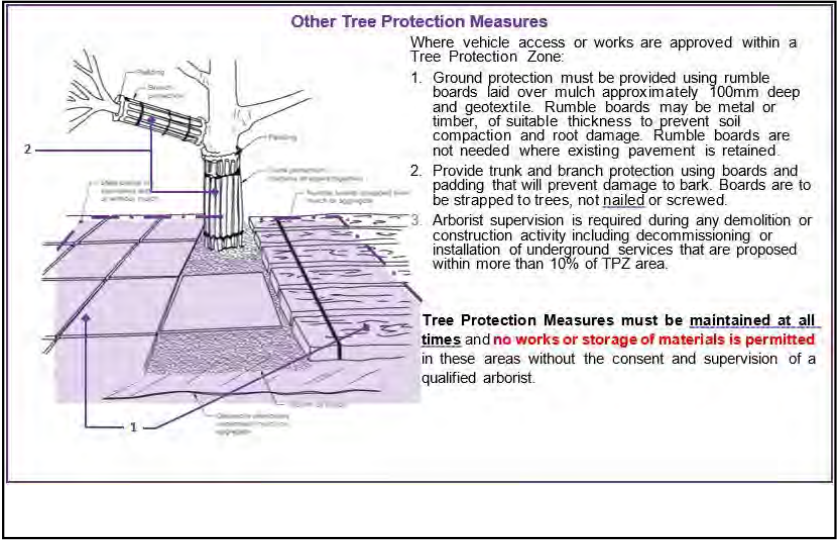


Figure 2. Examples of ground and trunk protection that can be implemented where fenced tree protection zones are not feasible.



Figure 3. An example of suitable ground protection system for use where exclusion fencing is not feasible. This system includes 3 layers of ground protection: Geofabric, crushed rock and perforated bog mats. These areas can be used as access ways for workers and light vehicles but remain tree protection zones where heavy machinery, storage and stockpiling are prohibited.

ADVERTISED
PLAN

This copied document to be made available for the sole purpose of enabling its consideration and review as part of a planning process under the Planning and Environment Act 1987. The document must not be used for any purpose which may breach any copyright

ROOT MANAGEMENT

- The Project Arborist must be contacted if any roots >40mm Ø are uncovered during work activities require removal. Root pruning must be undertaken or inspected by the Project Arborist; pruning must be done so with a pair of clean, sharp secateurs, loppers or handsaw with a final cut to undamaged wood. It is not acceptable for roots within the tree's TPZ to be 'pruned' with machinery, such as backhoes or excavators.
- Pruning wounds are not to be treated with dressings or paints.
- Exposed roots are to be covered by topsoil within 24 hours of exposure. Temporary root protection should be installed over roots if exposed for >24 hours. This may include jute mesh or hessian sheeting as multiple layers over exposed roots and excavated soil profile, extending to the full depth of the root zone. Root protection sheeting should be pegged in place and kept moist during the period that the root zone is exposed.

DEEP WATERING

- Apply water slowly, with drip irrigation or sprinkler system to at least the entire Tree Protection Zone, and ideally canopy dripline + 1m.
- Target depth of water penetration is 400-500mm. Soil should be moist to this depth, but not saturated. Watering should be undertaken weekly, but frequency may need to be adjusted depending on soil moisture levels.
- A tubular steel soil sampler, roughly 60cm in length, is ideal for checking soil moisture at depth.
- Water during the cooler parts of the day, preferably early morning or evenings.
- Check soil moisture frequently to ensure soil is sufficiently moist and NOT waterlogged.
- Indicative water requirement is 1.6L per cm of trunk diameter (but amount will vary depending on season, soil, TPZ area, and site conditions).

COORDINATE REFERENCE SYSTEM
EPSG:28355 | GDA 2020 MGA Zone 55



ABN: 95 080 021 610
TEL: 1300 656 926

TREELOGIC PTY LTD
4 / 21 Eugene Tee
Ringwood, VIC
Australia 3134



LEGEND

tree data
all_trees status

- P** Protect
- X** Remove
- Tree Protection Fencing
- Ground Buffering
- Tree groups
- Low
- easements
- roads

Notional Root Zone
Structural Root Zone

APPENDIX 2

TREE PROTECTION PLAN
Refer to Arboricultural Impact
Assessment report

PROJECT

2 to 6 LAMPARD ROAD,
DROUIN

TL REF.
13416

MAP NO.
1/1

CLIENT
Housing Choices
Australia

DATE
2026-06-02

DATA SOURCES

Ground Floor GA Plan. Prepared by
Lian Architects. Proj: HC02. Dwg: A004
Rev T1. Date: 24/3/2026

TREE LOCATION DISCLAIMER

Tree locations are derived from Feature
Survey Plan

COORDINATE REFERENCE SYSTEM
EPSG:28355 | GDA 94 MGA Zone 55



TREELOGIC PTY LTD
ABN: 95 080 021 610
TEL: 1300 656 926

4 / 21 Eugene Tce
Ringwood, VIC
Australia 3134



This copied document to be made available
for the sole purpose of enabling
its consideration and review as
part of a planning process under the
Planning and Environment Act 1987.
The document must not be used for any
purpose which may breach any
copyright

ADVERTISED
PLAN

Project Arborist must
* Meet with site manager to be
inducted as the Project
Arborist and convey the
importance of implementing
the Tree Protection Plan (TPP)
to ensure no damage occurs to
Heritage Trees 2-7 or any
other trees required to be
retained.
* The site manager must then
ensure all staff & contractors
engaged on the build are also
informed about the need to
comply with the TPP.
* Meet with pruning contractor
& site manager about canopy
pruning requirements.
* Supervise excavation of
balcony footprints where they
extend into NRZ of Trees 2 to
7. Refer to TPMP-V3 (17/4/26)
• Supervise the scraping of the
soil surface for permeable
pavements extending through
the NRZs of Elm Trees 4 & 5
as well as Tree 8.
• Supervise excavation for the
new driveway crossover within
the NRZ of Trees 8 & 9.
• Supervise excavation of
fence post in SRZ of trees 36 -
39



Tree Protection Zone signage
must be attached to each face of
any tree protection fencing


LEGEND

tree data
all_trees status

P Protect
X Remove

Tree groups
Low

--- easements
roads
Canopy encroachment %



APPENDIX 2
TREE PROTECTION PLAN
Refer to Arboricultural Impact
Assessment report & Tree
Protection Specifications

PROJECT
2 to 6 LAMPARD ROAD,
DROUIN

TL REF.
13416

MAP NO.
1 / 1

CLIENT
Housing Choices
Australia

DATE
2026-06-03

DATA SOURCES
Ground Floor GA Plan. Prepared by
Lian Architects. Proj: HC02. Dwg:
TP100 Rev P. Date: 25/05/2026

TREE LOCATION DISCLAIMER
Tree locations are derived from Feature
Survey Plan

COORDINATE REFERENCE SYSTEM
EPSG:28355 | GDA 94 MGA Zone 55

0 4 8m

TREELOGIC PTY LTD
ABN: 95 080 021 610
TEL: 1300 656 926

4 / 21 Eugene Tce
Ringwood, VIC
Australia 3134




Project Arborist must

- * Meet with the pruning contractor & site manager about canopy pruning requirements.
- * All pruning must be completed by suitably and experienced & qualified arborist (minimum AQF Cert 3- Arboriculture) complying with Australian Standard - Pruning of Amenity trees (AS4373-2007).
- * The final location of appropriate target pruning will be determined by the pruning arborist based on their best judgement of branching and weight distribution once they have accessed the tree for pruning purposes.
- * Pruning must be completed in a controlled manner to avoid damaging any trees that are required to be retained as well as property (fences) or impeding the movement of traffic on Main South Road or Lampard Road.
- * Climbing spikes must not be used to climb a tree for pruning purposes only. specify the extent of pruning



Tree Protection Zone signage must be attached to each face of any tree protection fencing

This copied document to be made available for the sole purpose of enabling its consideration and review as part of a planning process under the Planning and Environment Act 1987. The document must not be used for any purpose which may breach any copyright

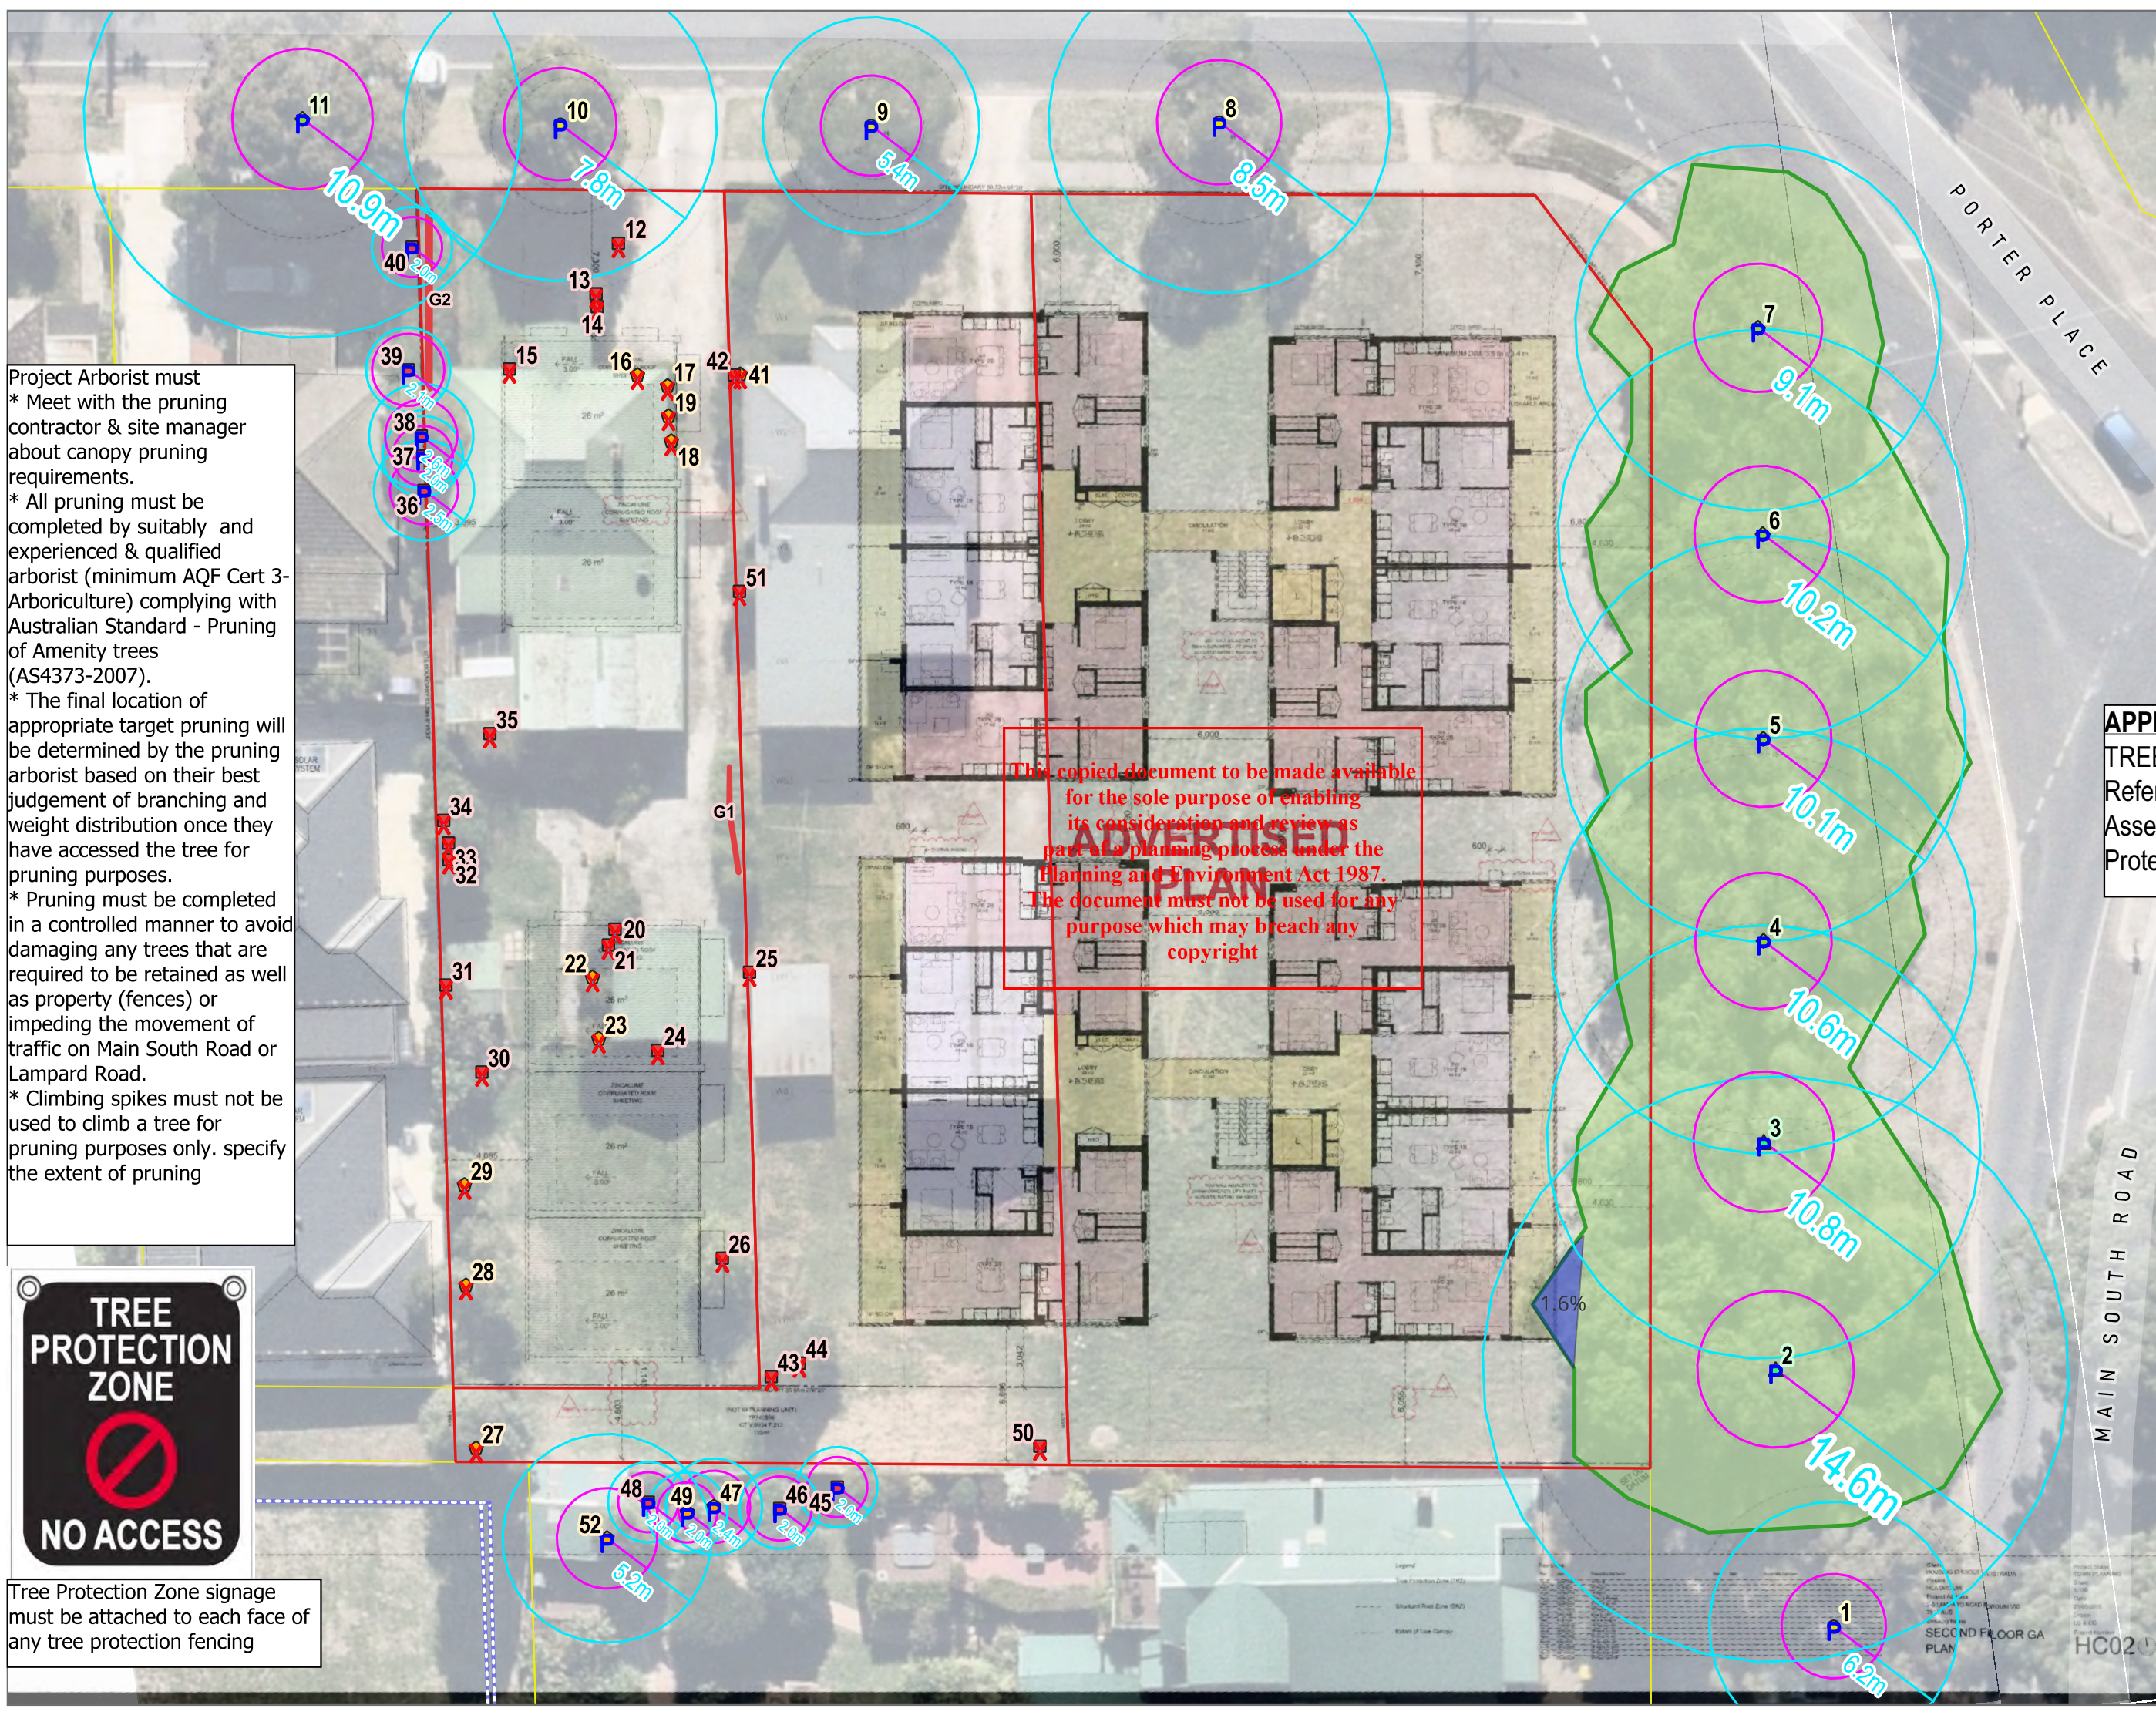

LEGEND

tree data
all_trees status

P Protect

Protection Measures

Arborist Supervision

Ground Protection

Tree Protection Fencing

Tree groups

Low

easements

roads

IMPACTS 260602

NRZ Minor (<10%)

NRZ Moderate (10–20%)

SRZ impacted

Notional Root Zone
 Structural Root Zone

APPENDIX 2

TREE PROTECTION PLAN
Refer to Arboricultural Impact
Assessment report & Tree
Protection Specifications

PROJECT

2 to 6 LAMPARD ROAD,
DROUIN

TL REF.

13416

MAP NO.

1/1

CLIENT

Housing Choices
Australia

DATE

2026-06-11

DATA SOURCES

Ground Floor GA Plan. Prepared by
Lian Architects. Proj: HC02. Dwg:
TP100 Rev P. Date: 25/05/2026

TREE LOCATION DISCLAIMER

Tree locations are derived from Feature
Survey Plan

COORDINATE REFERENCE SYSTEM

EPSG:28355 | GDA 94 MGA Zone 55



TREELOGIC PTY LTD

ABN: 95 080 021 610
TEL: 1300 656 926

4/21 Eugene Tce
Ringwood, VIC
Australia 3134



Project Arborist must

- * Meet with site manager to be inducted as the Project Arborist and convey the importance of implementing the Tree Protection Plan (TPP) to ensure no damage occurs to Heritage Trees 2-7 or any other trees required to be retained.
- * The site manager must then ensure all staff & contractors engaged on the build are also informed about the need to comply with the TPP.
- * Meet with pruning contractor & site manager about canopy pruning requirements.
- * Supervise excavation of balcony footprints where they extend into NRZ of Trees 2 to 7. Refer to TPMP-V3 (17/4/26)
- Supervise the scraping of the soil surface for permeable pavements extending through the NRZs of Elm Trees 4 & 5 as well as Tree 8.
- Supervise excavation for the new driveway crossover within the NRZ of Trees 8 & 9.
- Supervise excavation of fence post in SRZ of trees 36 - 39
- Meet with Landscaper to confirm hand weeding & planting of 140mm pot size only.



Tree Protection Zone signage must be attached to each face of any tree protection fencing

This copied document to be made available for the sole purpose of enabling its consideration and review as part of a planning process under the Planning and Environment Act 1987. The document must not be used for any purpose which may breach any copyright

ADVERTISED
PLAN
